


Works Notice

May 2021

Roma Street station construction update

Piling for the new station entry building is finishing and excavation of its 20m-deep shaft has now started. Excavation of the new services building is now more than 30% complete.

Underground work continues in the new station cavern and the team is preparing for the Tunnel Boring Machines (TBMs) to arrive in the coming months.

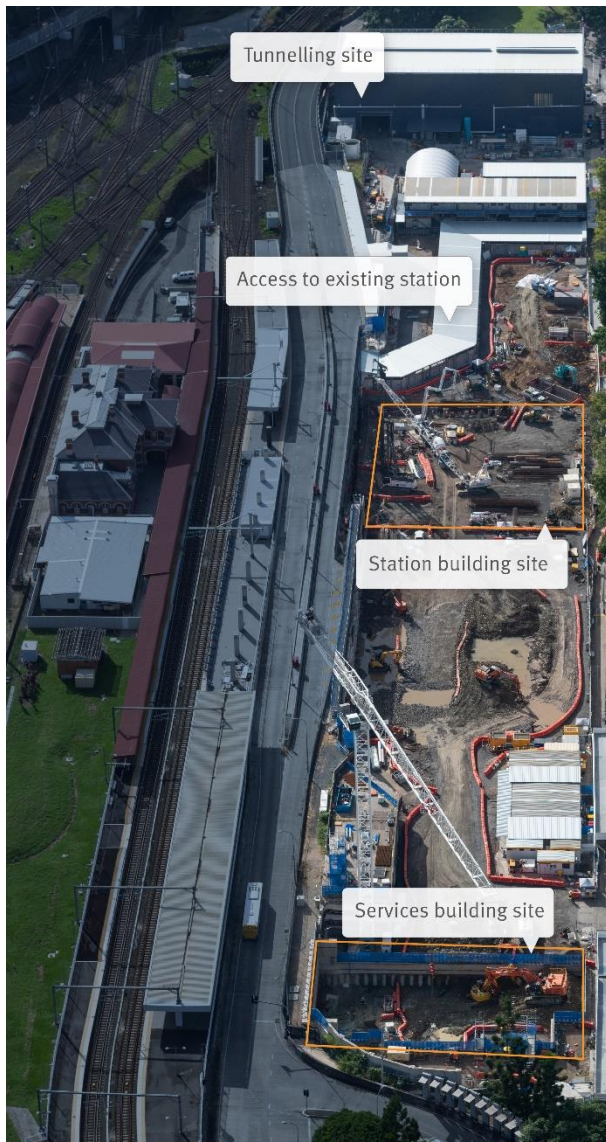

Aerial view of the Roma Street station construction site.



View of the new underground station cavern beneath the existing Roma Street station.



Preparing to concrete the walls of the new station cavern.

Station building site

Opposite Makerston Street



Stormwater main relocation

Ongoing to May 2021

- Night and weekend work to relocate an existing underground stormwater main service in Roma Street.
- Ongoing progress updates will continue to be provided.

Excavation and ground support

Ongoing

- Constructing a concrete beam to connect the bored piles.
- Excavating the shaft, installing ground support anchors and shotcrete.
- Loading and removing excavated material with trucks.
- Mobilising and installing a tower crane to support excavation.
- Installing micro-piles and ground anchors beneath the Inner Northern Busway.

Some activities in the new station building construction area will be undertaken outside of standard construction hours. Activities include constructing the capping beam, excavating and transporting material from site, installing ground support anchors and shotcrete within the shaft. More information will be provided to surrounding businesses and residents before night work starts.

Services building site

Opposite Garrick Street



Excavation and ground support

Ongoing

- Excavating the shaft and progressively installing ground support anchors and shotcrete.
- Loading and removing excavated material with trucks.

Some activities in the new services building construction area will be undertaken outside of standard construction hours. Activities include excavating and transporting material from site, installing ground support anchors and shotcrete within the shaft. More information will be provided to surrounding businesses and residents before night work starts.

Tunnelling site

Acoustic shed, corner of Roma Street and Parkland Boulevard



Underground excavation

Ongoing

- Excavating passenger access tunnels (known as adits) and the station cavern by roadheader.
- Loading and removing excavated material with trucks.
- Intermittently conducting controlled production blasts within the station cavern and adits.

Local streets

Roma Street between Countess Street and Parkland Boulevard



Site establishment and services inspection

Ongoing

- Installing site access gates and gantries.
- Groundwater monitoring.
- Inspecting and relocating underground services around the Roma Street construction site.

What to expect

- Construction activity with potential for an increase in noise, dust, vibration, truck movements and workers.
- Construction impact mitigation activities such as street sweepers, dust suppression and hoarding installation.
- Temporary traffic and pedestrian changes on Roma Street and surrounding streets.
- Work is subject to relevant approvals and suitable weather conditions.

Work hours



Standard construction hours

Standard construction hours are 6:30am to 6:30pm, Monday to Saturday.



Out of hours works

Some activities will be completed out of normal construction hours due to traffic permits, safety requirements and construction methodology. Nearby residents will be notified in advance via letterbox drop or a poster in the apartment building mail room.



24 hours

Tunnelling and tunnelling support activities are undertaken 24 hours a day within the acoustic shed.

1800 010 875

crossriverrail@cbgujv.com.au

crossriverrail.qld.gov.au



If you need an interpreter to assist you in understanding this document, please call the Translating and Interpreting Service (TIS National) on 131 450 and request to be transferred to Multicultural Affairs Queensland on 13 QGOV (13 74 68)

